



Government of South Australia

Department for Infrastructure
and Transport



Department for Infrastructure and Transport

Construction Sector Industry Briefing

Tuesday, 4 August 2020

Welcome to Country

The Department for Infrastructure and Transport acknowledges the Kurna people of whose land we meet on today. We also pay our respects to their Elders past and present and extend that respect to other Aboriginal and Torres Strait Islander people who are present today.



**Andrew Excell | Director, Network
and Investment Strategy**



Presenters

- Hon. Corey Wingard MP
Minister for Infrastructure and Transport
- Mr. Tony Braxton-Smith
Chief Executive
- Mr. Wayne Buckerfield
Executive Director, Transport Planning and Program Development
- Ms. Susana Fueyo
Executive Director, North-South Corridor Program Delivery Office
- Mr. Jon Whelan
Executive Director, Transport Project Delivery
- Mr. Simon Morony
Executive Director, Across Government Services



Hon. Corey Wingard MP

Minister for Infrastructure and Transport



Mr. Tony Braxton-Smith

Chief Executive

Departmental update

Overview



Target Master Schedule

Project Management Toolkit

Procurement Reforms

Delivery Models

COVID-19 Safety and Stimulus Program

Departmental update

Key priorities





Mr. Wayne Buckerfield

Executive Director, Transport Planning and Program Development

Currently over \$30 million of active planning Studies focused on improvements at over 100 locations across the State.

Upcoming studies to be released for tender in coming months, to address priorities in the 20 Year State Infrastructure Strategy, include:


- Four packages totalling circa \$10 million to undertake:
 - network plans and corridor studies; and
 - detailed planning and business case development.
- Will be delivered through Integrated Planning Partner Contracts.


Transport modelling

- Industry Engagement and collaboration on improvements to modelling tools and approaches.

Other procurements

- Survey, geotechnical investigations, pavement design and heritage assessments (to be released throughout the year to support projects).

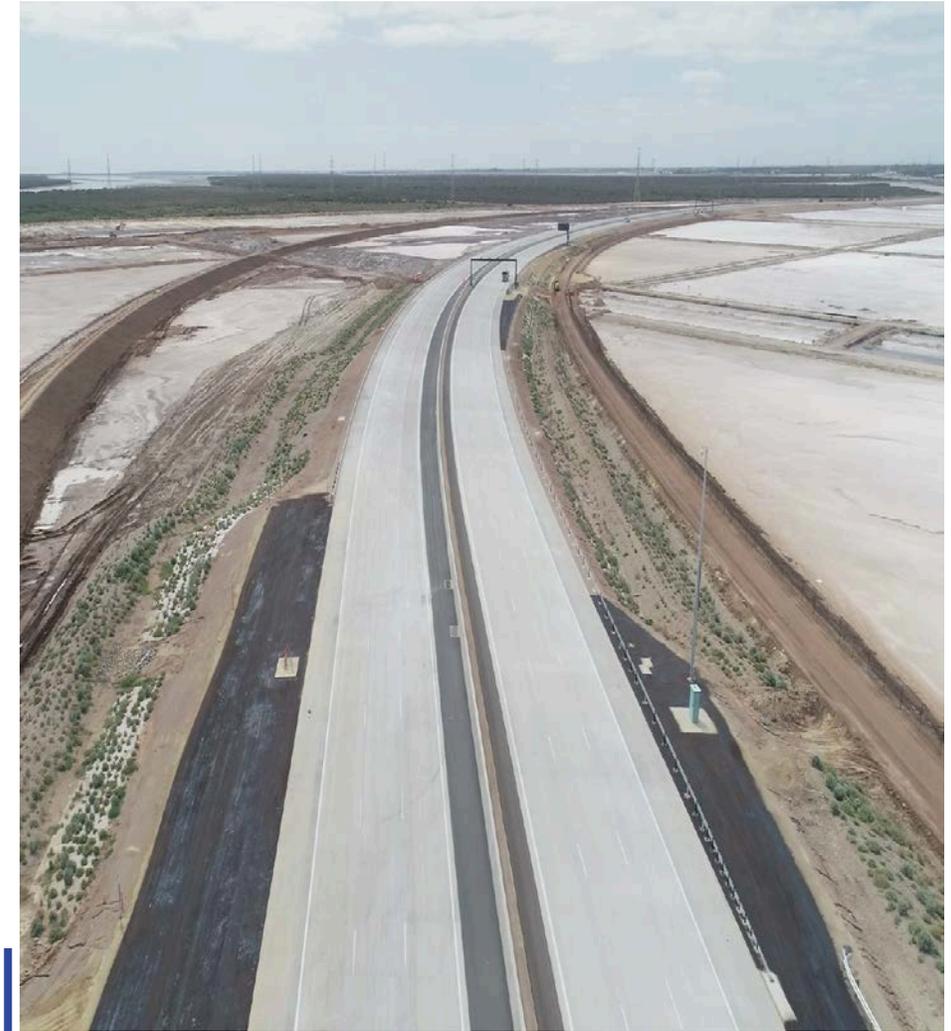



Ms. Susana Fueyo

Executive Director, North-South
Corridor Program Delivery Office

North-South Corridor

River Torrens to Darlington (T2D) is the largest and most complex infrastructure project ever delivered in SA.

10.5 kilometre stretch of roadway - the final stage of the multi-billion NSC.

OUTCOME

78 kilometre non-stop motorway connecting the Northern and Southern suburbs and providing a vital strategic link for motorists and the freight industry.

Project Overview



\$5.4 billion towards the project



Job creation



Congestion cost savings

North-South Corridor

Project Options

Option 1: Open motorway option


A combination of at-grade, short tunnels, lowered and elevated motorway as seen on other parts of the North-South Corridor.



Option 2: Hybrid option

Has the same at-grade and lowered motorway design between James Congdon Drive (Mile End South) and Edward Street (Edwardstown) with tunnels at the northern and southern ends.

North-South Corridor Timeline

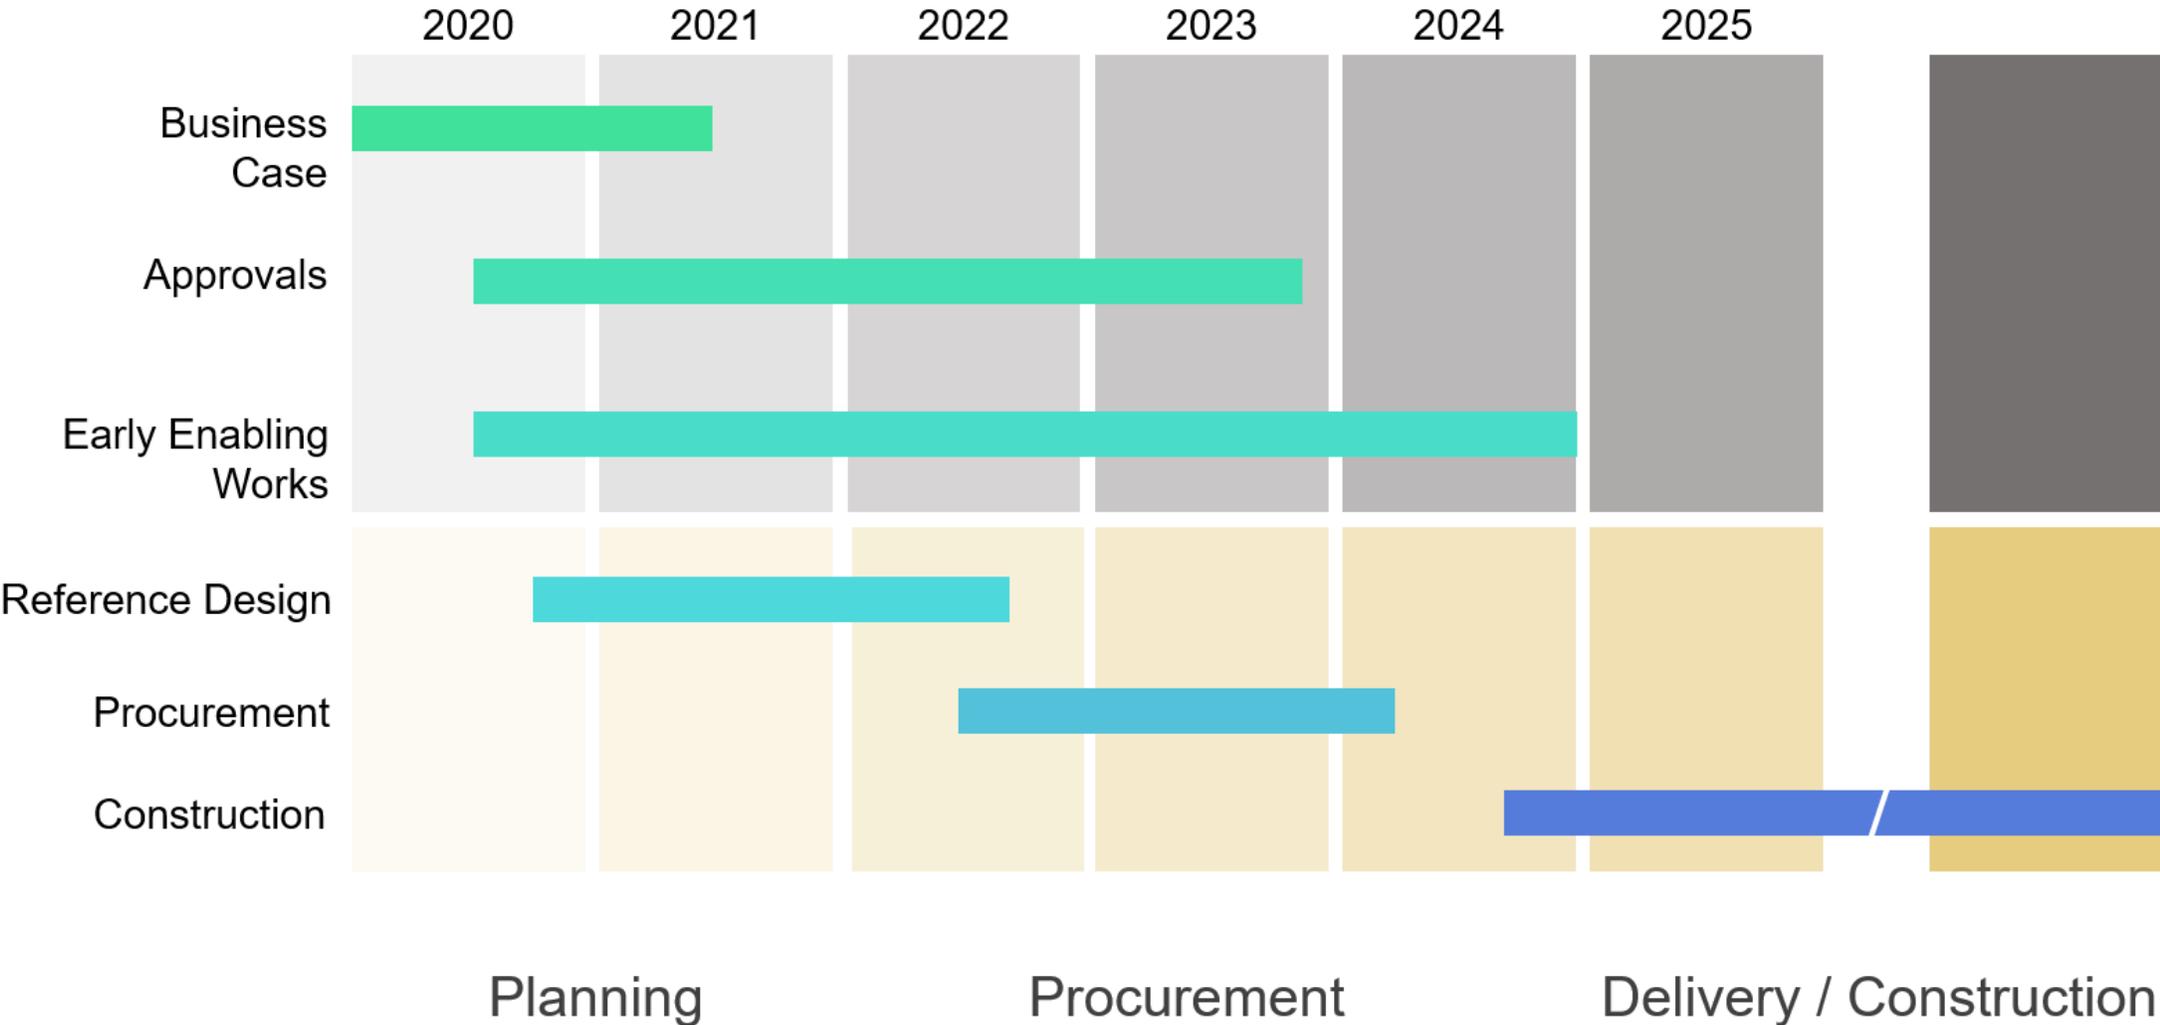

North-South Corridor

Industry Participation



Attract industry-best

Partnering with dynamic, collaborative and industry leaders to deliver outstanding results and maximise economic benefits for SA.



Maximise local content

Maximising the use of local industries to achieve the project objectives through innovation and collaboration.



Sustainable Growth

Creating a legacy project by promoting sustainable business growth and expanding opportunities for local industry.

North-South Corridor

Overall Procurement Schedule


Procurement	Approx. Value	Approach	2020			2021				2022				2023
			Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	+
✓ Ground investigations (Stage 1)	■	RFT		■										
Market sounding	■	RFQ		■										
Reference Design	■	RFP			■	■								
Master Advisory Services	■	RFP			■	■								
Planning of off road intersections	■	RFT				■	■							
Ground investigations (Stage 2)	■	RFT					■	■						
Off road intersections	■	TBD								■	■			
Main works head contract	■	TBD											■	■

Estimated Procurement Value: ■ \$0 - \$5m / ■ >\$5m - \$20m / ■ > \$20m


Note: all information is indicative and subject to change.

Our Procurement Objectives

Maximise participation



Agile procurement



Partner and collaborate

Reference design for the NSC



Seeking an industry partner to develop the Reference Design for the NSC.



One stage procurement process

- RFP to award a successful Proponent.



10 week procurement process

- RFP call date: mid-August 2020
- RFP close date: mid-September 2020
- Anticipated contract award: mid-October 2020
- Contract term: 12 months



Master Advisory Services to support the NSC

Scope

Seeking an industry partner that brings in a dynamic team comprising resources with technical expertise and demonstrated capability to support the Department in development of the project requirements and constraints.

Strategy

One stage procurement process

- RFP to award a successful Proponent.


Timing

To be confirmed pending the Registration of Interest.



Registration of Interest
5 Aug 2020

A graphic consisting of two concentric circles. The inner circle is a vibrant blue and contains the text 'Registration of Interest' and '5 Aug 2020' in a bold, white, sans-serif font. The outer circle is a lighter, pale blue and is empty.

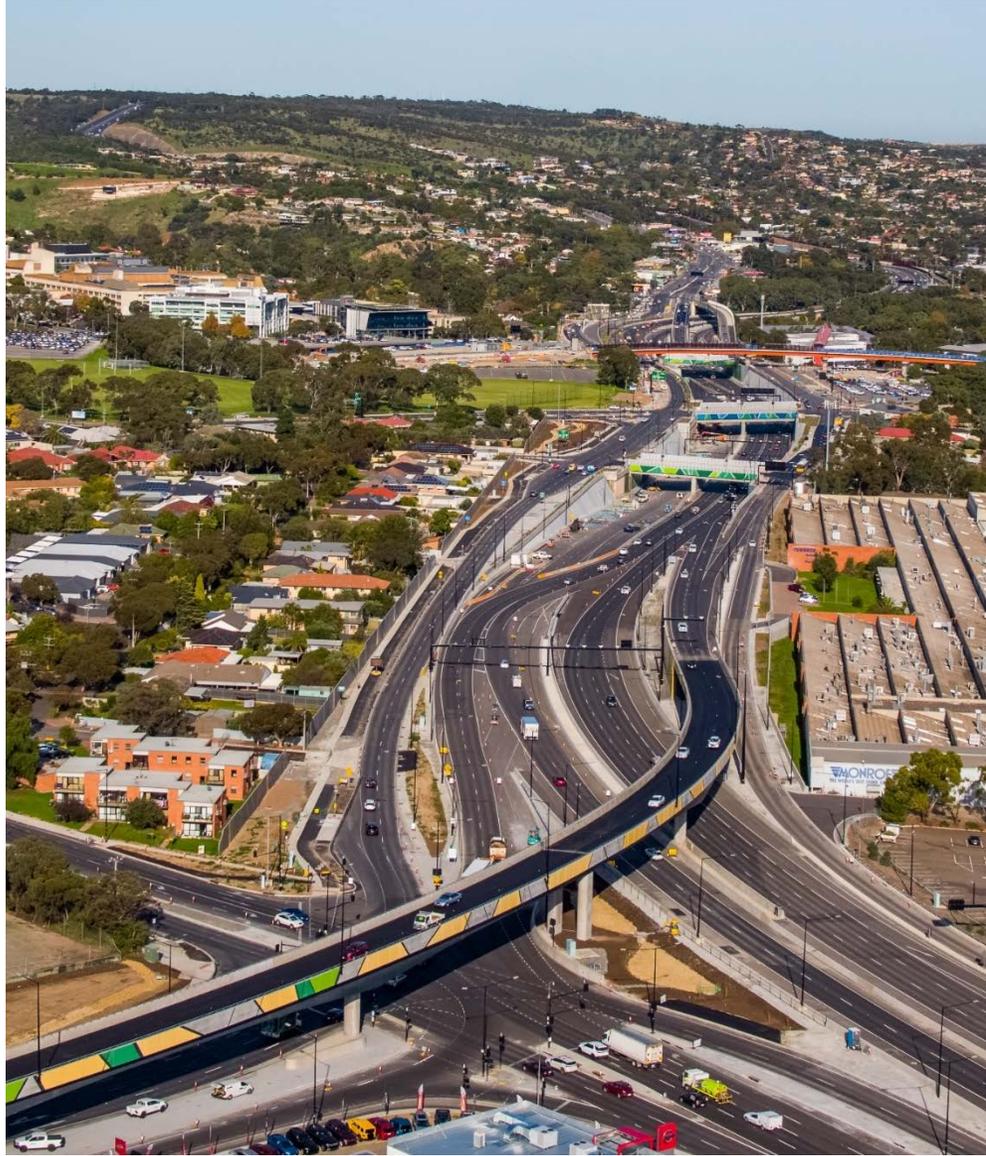

Mr. Jon Whelan

Executive Director, Transport
Project Delivery

Transport Project Delivery

The 2020-2021 budget for Transport Project Delivery is approximately \$1.2 billion, which includes \$105 million in minor works through the Department's Annual Program.



Transport Project Delivery

Update on Current Capital Works

Project	Project value	Status
Regency Road to Pym Street (Alliance)	\$354.3m	<ul style="list-style-type: none">Alliance contract awarded in July 2019. Construction works commenced Q4 2019.
Port Wakefield to Port Augusta Alliance (Alliance)	\$290m	<ul style="list-style-type: none">Contract awarded March 2020. Construction works to commence in Q3 2020.
Gawler Rail Electrification Project	\$615m	<ul style="list-style-type: none">Major works completion late 2021.



Artist impression of the Joy Baluch AM Bridge Duplication



JOY BALUCH AM BRIDGE DUPLICATION PROJECT

Aerial overview and artist's impression of the Joy Baluch AM Bridge Duplication

Transport Project Delivery

Investing over **\$330 million** to upgrade metropolitan intersections, improve safety and decrease travel times for motorists.



Congestion Busting Infrastructure Metropolitan Congestion Initiative

No.	Project	Project value	Proposed delivery model	Anticipated procurement commencement
1	Main North Road / Kings Road / McIntyre Road intersection	\$13m	Construct only	EOI Released 14/07/2020
2	Goodwood Road / Springbank Road / Daws Road intersection	\$60m	Construct only	EOI Released 14/07/2020
3	Main North Road / Nottage Terrace intersection	\$19m	Construct only	Sept 2020
4	Cross Road / Fullarton Road intersection	\$61m	D&C	Dec 2020
5	Glen Osmond Road / Fullarton Road intersection	\$35m	D&C	Dec 2020
6	Portrush Road / Magill Road intersection	\$98m	Construct only	Dec 2020
7	Grand Junction Road / Hampstead Road / Briens Road intersection	\$19m	Construct only	Sept 2020
8	Old Belair Road / James Road intersection	\$20m	D&C / Construct only	Dec 2020
9	Woodside Rd / Old Princes Highway / Saleyard Rd, Nairne - Installation of a Roundabout	\$10m	Construct only	Q1 2021

Transport Project Delivery

Congestion Busting Infrastructure Grade Separations

Over **\$400 million** to remove two key level crossings along the Seaford and Gawler train lines in order to ease congestion and cut travel times.

Project	Project value	Proposed delivery model	Anticipated procurement commencement
Torrens Road (Ovingham) Level Crossing Upgrade	\$231m	Alliance	<ul style="list-style-type: none">• RFP Closed 18 June 2020• Construction work expected to commence Q2 2021
Brighton Road (Hove) Level Crossing Upgrade	\$171m	Alliance	<ul style="list-style-type: none">• Late Q1 2021



Transport Project Delivery

Safety upgrades on right country roads

Investing up to **\$70 million** to upgrade 8 country roads to enable the speed limit to be reinstated to 110km/h.

Works may include:

- shoulder sealing
- resealing
- vegetation removal
- installation of safety barriers
- wide centre line treatment (Riddoch Highway)
- audio tactile line marking



No.	Regional Road Projects and Transport Infrastructure Upgrades	Approx. contract value	Works to commence
1	Andamooka Road (Andamooka to Olympic Dam)	\$5m	Completed
2	Browns Well Highway (Loxton to Pinnaroo)	\$15m	August 2020
3	Carpenter Rocks Roads (Carpenter Rocks to Mount Gambier)	\$1m	Completed
4	Clay Wells Road (Southern Ports Highway to Callendale)	\$8m	August 2020
5	Cleve Road (Cleve to Kimba)	\$9m	Works underway
6	Goyder Highway (Crystal Brook to Gulnare)	\$3m	Completed
7	Ngarkat Highway (Pinnaroo to Bordertown)	\$17m	August 2020
8	Riddoch Highway (Mount Gambier to Port MacDonnell)	\$3m	Late 2020

Project	Project value	Proposed delivery model	Anticipated procurement commencement
Lower Eyre Peninsula improvements <ul style="list-style-type: none"> • Overtaking lanes (5) • Intersection enhancements • Shoulder sealing (approx. 35 km) • Pavement rehabilitation • Minor Bridge rectification works • ATLM, Barrier & Signage Upgrades 	\$32m	Various Multiple Packages	Q3 2020 to Q2 2022
Eyre Highway - Port Augusta to Perth (SA section only) <ul style="list-style-type: none"> • Overtaking lanes (2) • Kimba Level Crossing intersection re-alignment • Intersection upgrades (2) • Rest areas (3) • Shoulder sealing (approx. 110 km) • Pavement rehabilitation • ATLM & signage upgrade 	\$93m	Various Multiple Packages	Q4 2020 to Q3 2022
Sturt Highway (Renmark to Gawler) <ul style="list-style-type: none"> • Overtaking lanes (5) • Duplication works near Renmark • Intersection upgrades (4) • Rest areas (6) • Shoulder sealing (approx. 20 km) • Pavement rehabilitation • ATLM, barrier & signage upgrade 	\$87.5m	Various Multiple Packages	Q4 2020 to Q4 2022
Barrier Highway - Cockburn to Burra <ul style="list-style-type: none"> • Intersection upgrades (2) • Rest Areas (4) • Shoulder sealing (approx. 95 km) • Pavement rehabilitation • Bridge rectification works • ATLM, barriers & signage upgrade 	\$62.5m	Various	Q4 2020 to Q4 2022

Road Corridor Improvements Roads of Strategic Importance

Investing over **\$275 million** to improve productivity, safety and maintenance.


Multiple contract works may include:

- shoulder sealing;
- pavement rehabilitation;
- road duplication;
- bridge upgrades;
- overtaking lanes;
- installation of safety barriers;
- audio tactile line marking;
- intersection upgrades; and
- rest areas.



Transport Project Delivery

Investing over **\$230 million** to improve regional productivity and developing safer country roads.

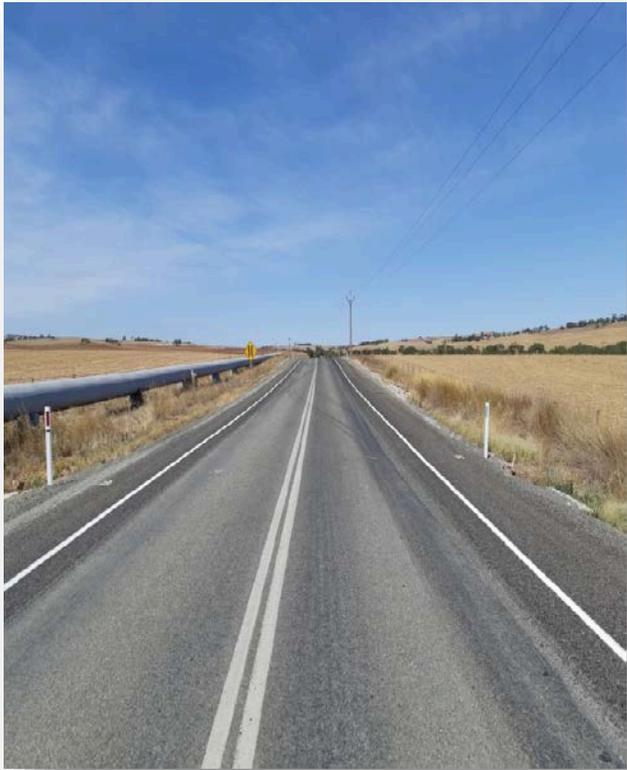

Regional Road Projects and Transport Infrastructure Upgrades	Project value	Proposed delivery model	Anticipated procurement commencement
Horrocks Highway <ul style="list-style-type: none"> • Overtaking lanes (4) • Shoulder sealing (approx. 50 km) • Pavement rehabilitation • Gladstone Rail Level Crossing upgrade • Spring Creek Bridge upgrade • Hutt River Bridge upgrade • Little Spring Creek Bridge upgrade • ATLM and Signage upgrade 	\$55m	Various Multiple Packages	Q4 2020 to Q1 2022
Overtaking Lanes (7 in total) <ul style="list-style-type: none"> • Victor Harbor Road • Long Valley Road • Lincoln Highway (2) • Riddoch Highway (3) 	\$32.9m	Various Multiple Packages	Q1 2021 to Q4 2021
Princes Highway Corridor Improvements <ul style="list-style-type: none"> • Overtaking lanes (5) • Shoulder sealing (approx. 60km) • Pavement rehabilitation • Princes Highway Bridge upgrades • Intersection upgrades and Rest Areas between Kingston and Mt Gambier • Intersection of Princes Hwy and Dukes Hwy, Tailem Bend • ATLM, Signage and Safety Barrier 	\$141.5m	Various Multiple Packages	Q3 2021 to Q1 2023

Transport Project Delivery

Targeted Road Safety Works (Stimulus Package)

Investing up to **\$59.5 million** to address road safety and fatigue management issues.

Works may include:

- shoulder sealing;
- sealing local road approaches and minor junction improvements;
- road lighting improvements;
- installation of safety barriers;
- activated safety signing and variable speed limit; and
- audio tactile line marking.

No.	Project	Project value	Proposed delivery model	Anticipated procurement commencement
1	Safety Barrier Program	\$10m	Construct Only	Multiple Packages Q4 2020 to Q1 2021
2	Long Valley Road Safety Improvements <ul style="list-style-type: none"> • localised widening • shoulder sealing • intersection treatments • safety barriers and sight distance improvements 	\$6m	Construct Only	Multiple Packages Q4 2020 to Q2 2021
3	Activated Safety Signing on SE Freeway	\$4m	Design & Construct	Q3 2020
4	Audio Tactile Line Marking	\$10m	Construct Only	Multiple Packages Sept 2020 to Q1 2021
5	Shoulder Sealing	\$5m	Construct Only	Two Packages Sept 2020
6	Road Lighting Improvements	\$8.5m	Construct Only	Multiple Packages Sept 2020 to Apr 2021
7	Variable Speed Limit Signs	\$1m	Construct Only	Q1 2021
8	Sealing Local Road Approaches & Minor Junction Improvements	\$10m	Construct Only	Multiple Packages Sep 2020 to Mid 2021
9	Median Wire Rope - Dukes Highway	\$5m	Construct Only	Multiple Packages Q1 2021 to Q2 2021

Transport Project Delivery

Infrastructure Investment Program (Stimulus Package)

Investing up to **\$85 million** to improve regional productivity, safety and maintenance.

Works may include:

- upgrade of safety, communications and electrical systems in the Heysen Tunnel;
- shoulder sealing;
- resealing/resurfacing;
- bridge widening and bridge safety barriers (between Murray Bridge and Annadale); and
- installation of safety barriers.



Project	Project value	Proposed delivery model	Anticipated procurement commencement
Heysen Tunnel refit and safety upgrade	\$15m	Design & Construct	Dec 2020
Regional Road Network Package <ul style="list-style-type: none"> • will target safety enhancements such as pavement treatments and shoulder sealing to benefit the freight industry and regional communities across South Australia. <ul style="list-style-type: none"> - Stuart Highway - Dukes Highway - Riddoch Highway - Copper coast Highway - Maitland Road - Victor Harbor Road - Thiele Highway - Yorke Highway 	\$52m	Construct only	Multiple Packages (Asphalt, Spray Seal and Pavement Rehabilitation) First Package Sept 2020 All Packages out by Feb 2021
Regional North-South Freight Route - Shoulder Sealing	\$6m	Construct only	Called Q3 2020 being assessed
Regional North-South Freight Route - Bridge Work	\$6m	Construct only	Feb 2021
Adventure Way and Innamincka Airport Access Road	\$6m	Construct only	In construction

Transport Project Delivery

Regional Road Projects and Transport Infrastructure Upgrades

The final stage of construction works to the **APY Lands Main Access Road** will upgrade approximately 32km of unsealed road, from Number Tanks to Mimili.

Project	Project value	Proposed delivery model	Anticipated procurement commencement
APY Lands Main Access Road Upgrade (Stage 2 C)	\$14m	Construct only	Q1 2021



Transport Project Delivery

Key Road Corridor Duplications

Main South Road duplication (Stage 1) - the duplication of approximately 10km, from south of Griffiths Drive in Seaford to Aldinga.

Victor Harbor Road duplication – the duplication between Main South Road and McLaren Vale, linking to the McLaren Vale Overpass.

Project	Project value	Proposed delivery model	Anticipated procurement commencement
Main South Road Duplication between Seaford and Aldinga (Stage 1)	\$287m	Alliance	Late Sept / early Oct 2020
Victor Harbor Road Duplication – Main South Road to McLaren Vale	\$92m		



Transport Project Delivery

New Sand Pumping System Largs Bay to West Beach (Funded by DEW)

Project Value	Proposed delivery model	Procurement
\$26.4m	Construct, Operate & Maintain	Q1 2021



Flagstaff Road Upgrade

Project Value	Proposed delivery model	Procurement	Anticipated Award
\$32.9m	ECI Construct only	RFP Stage 1 In tender assessment	Dec 2020



Transport Project Delivery

Granite Island Causeway

Project Value	Proposed delivery model	Anticipated procurement commencement	Anticipated Award
\$31.1m	ECI Design & Construct	RFP Stage 1 In tender assessment	Q4 2020

K I Ports Rebuild (Two new ferry ports Cape Jervis and Penneshaw)

Project value	Proposed delivery model	Anticipated procurement commencement
\$22m	Design & Construct	Q1 2021



Transport Project Delivery

Road Infrastructure Annual Program – Asphalt Works \$34.5 million

Project	Project value	Proposed Delivery Model	Anticipated procurement commencement
Asphalt Resurfacing on Sir Donald Bradman Drive (MTA)	\$3.5m	Construct only	On call
Asphalt Resurfacing of Fullarton Road / Taylors Road and Glen Osmond Road	\$4.m	Construct only	Aug 2020
Asphalt Resurfacing of Addison Road, Eastern Parade and Victoria Road	\$6.5m	Construct only	Aug 2020
Asphalt Resurfacing of Cormack Road and Churchill Road North	\$6.5m	Construct only	Aug 2020
Asphalt Resurfacing of five sites in the North Eastern Suburbs	\$6.5m	Construct only	Sept 2020
Asphalt Resurfacing in the North Metro Area	\$5.m	Construct only	Sept 2020
Asphalt Resurfacing on Grand Junction Road (Gallipoli Drive to Churchill Road)	\$2.5	Construct only	Dec 2020





Mr. Simon Morony

Executive Director, Across Government Services


Building Projects

Overview

Building Projects is responsible for delivering over \$3.2 billion of social infrastructure (building construction) projects on behalf of other State Government agencies.

Agencies serviced by Building Projects include:

- Department for Education
- SA Health – metropolitan and regional
- Department of Premier and Cabinet
- Metropolitan Fire Service
- Department Innovation and Skills
- Department for Correctional Services
- Adelaide Cemetery Authority
- Office of Recreation, Sport and Gaming
- West Beach Parks
- Department for Primary Industries and Regions

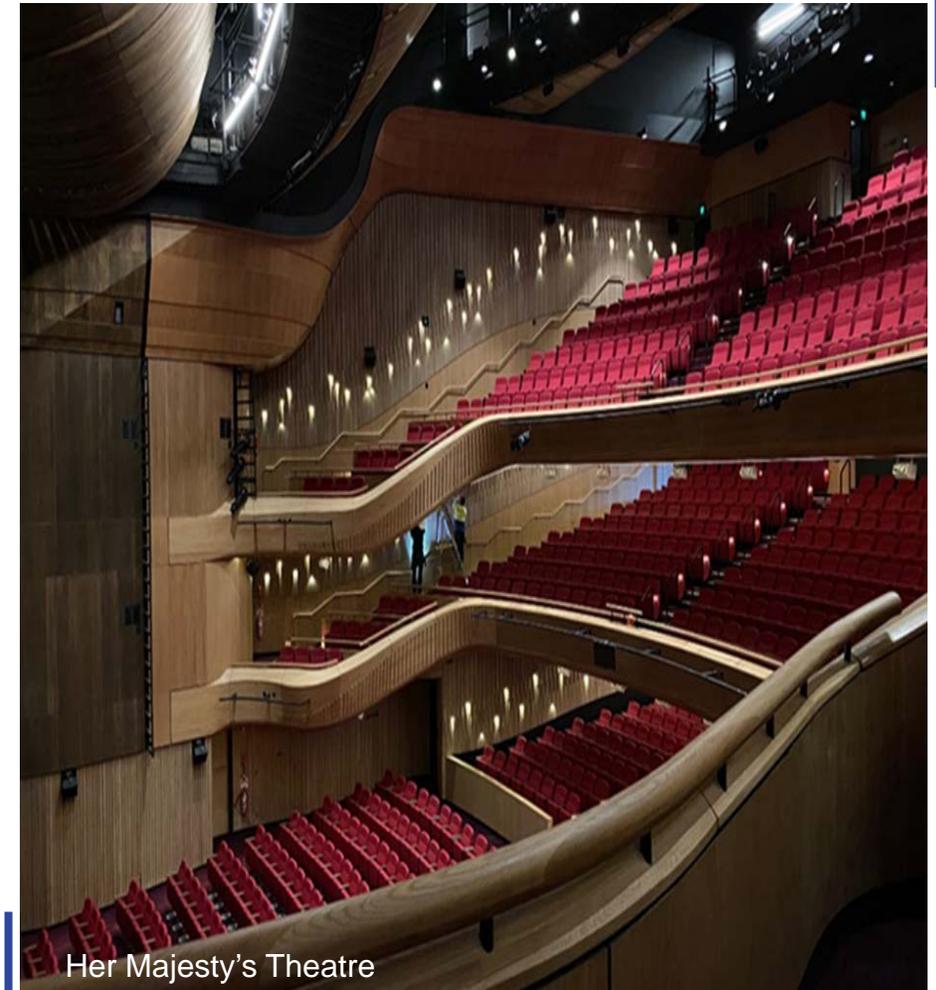



Building Projects

Upcoming tendering opportunities

(excluding Education Capital Works Program)

Under \$50m

Over \$50m

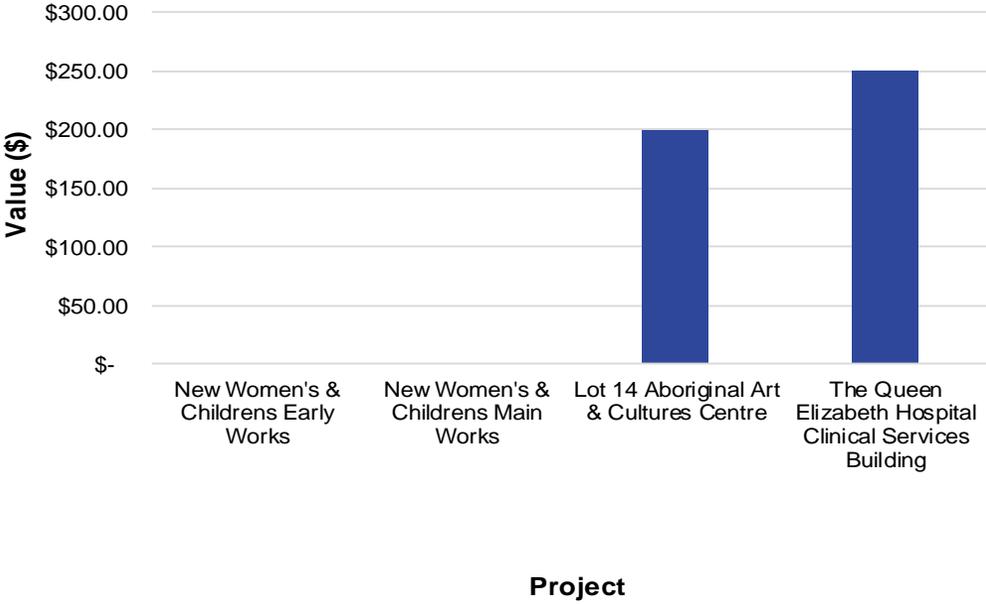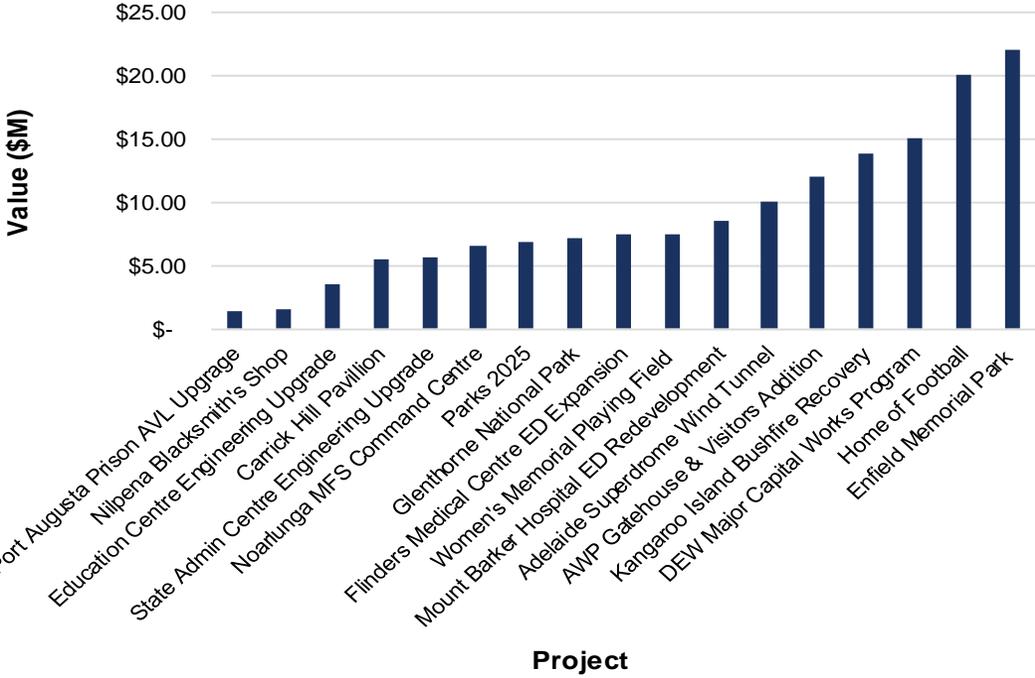

Building Projects

Department for Education overview

Building Projects is delivering 70 metro and regional school upgrades worth approximately \$750 million as part of the Department for Education's Capital Works Program. The program of works is being procured in three rounds, using either a Construct only or Design and Construct delivery model.

Education Capital Works Program – Round 1 & 2


Rounds 1 and 2 projects must be complete and ready for Year 7's to transition into high school for Term 1, 2022. Construction contract award for both rounds is nearing completion, with the remaining to be awarded over the next 4 months, and have a target completion of October 2021.

In conjunction with Building Projects' delivery the Department for Education are delivering a number of the Capital Works projects via a modular program.




Program status

Project phase – Round 1

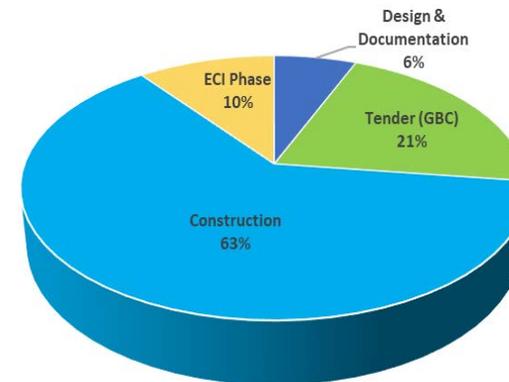

Project phase – Round 2

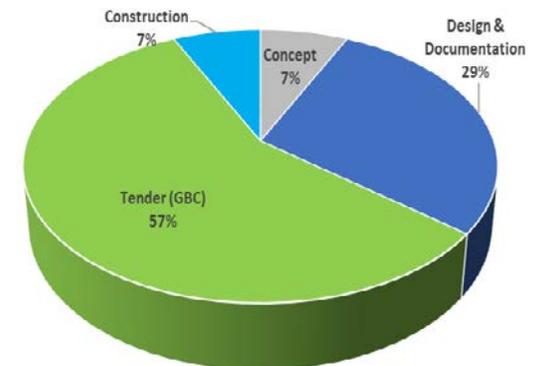

Building Projects

Department for Education upcoming opportunities

Education Capital Works Program – Round 3

Round 3 of the Education Capital Works program will see over **\$60 million** worth of upgrades to metropolitan and country Adelaide schools. Project values will range between \$5-\$10 million with a target completion of 2022/2023.

The program of works is mainly being procured using a Construct only delivery model with 1 likely to be D&C.

Proposed delivery models	Contract	Anticipated procurement commencement	Value of round	No. of projects	Completion Timeframe
Construct Only (1 likely to be D&C)	Designer	From Q3 2020	\$63m	11 Schools • 8 Metro • 3 Regional	2022/2023 (1 project late 2021)
	Builder	Early 2021			

A number of stimulus and maintenance backlog programs are also being delivered via Facilities Services and Spotless such as:

- **\$25 million** maintenance program: 159 projects across 116 sites.
- **\$25 million** maintenance program: up to 500 schools and pre-schools.

In conjunction with Building Projects' delivery the Department for Education are delivering a number of the Capital Works projects via a modular program.



Building Projects

Department for Health and Wellbeing upcoming opportunities

SA Health Metropolitan and Regional Works

Building Projects are currently delivering over **\$550 million** of project work within Adelaide's Metropolitan Hospitals, including projects currently in construction:

- Modbury Hospital (\$96m) (Managing Contractor)
- The Repat Health Precinct Reactivation (\$80m) (Managing Contractor)
- Lyell McEwin Hospital Emergency Department Expansion and Carpark (\$55.33) (Managing Contractor)
- Women's & Children's Hospital Sustainment Works (\$50m) (Managing Contractor)



Women's & Children's Hospital Sustainment Works

No.	Project	Proposed delivery model	Project value	Contract	Anticipated procurement commencement
1.	The Queen Elizabeth Hospital Redevelopment Stage 3 – Clinical Services Building (enabling package \$3.54m out for tender)	Managing Contractor or D&C	\$250m	Designer	Complete
				Builder	ROI Q4 2020 RFT Q1 2021
2.	SA Pathology Site Service Separation	Construct Only	\$6.4m	Designer	Complete
				Builder	Q3 2020
3.	Flinders Medical Centre Emergency Department Expansion	Construct Only	\$7.4m	Designer	Complete
				Builder	Q4 2020
4.	Mount Barker Hospital Emergency Department Redevelopment	Construct Only	\$8.6m	Designer	Complete
				Builder	Q1 2021
5.	SA Regional Hospitals Sustainment Works (over 10 years)	Construct Only	\$14m p.a	Designer	Ongoing opportunities
				Builder	

Building Projects

Department for Health and Wellbeing

New Women's and Children's Hospital



Completed

- Site selection (adjacent to the Royal Adelaide Hospital).
- \$550m State Government funding commitment (to continue planning).
- Key contracts have been awarded –architects, engineers, cost consultants and Final Business Case Consultant.



Next steps

- Consultation with clinicians to develop Functional Design Brief.
- Site access, RAH interface and services relocation investigations.
- Master Planning and Concept Design.
- Finalisation of recommended procurement delivery model.
- Identification of possible early works.

Building Projects

Department for Premier and Cabinet

Arts SA

Over **\$200 million** towards South Australia's cultural institutes including a new Aboriginal Art and Culture Centre to be built on the Renewal SA Lot 14 site.

No.	Project	Proposed delivery model	Project value	Contract	Anticipated procurement commencement
1.	Carrick Hill Pavillion	Construct only	\$5.5m	Designer	Complete
				Builder	Q2 2021
2.	Lot 14 Aboriginal Art and Culture Centre (AACC)	TBA	\$150m	Builder	RFT Q2 2021



Building Projects

Office of Recreation and Sport

Office of Recreation and Sport

Three separate projects to establish the State Sports Park as a world class sporting hub, as well as an upgrade at the Women's Memorial Playing Fields at St Mary's.

No.	Project	Proposed delivery model	Project value	Contract	Anticipated procurement commencement
1.	State Sports Park - Home of Football	Construct only	\$20m	Designer	Complete
				Builder	Q3 2020
2.	State Sports Park - Adelaide Super Drome Wind Tunnel Upgrade	Construct only	\$10m	Designer	Complete
				Builder	Q3 2020
3.	Women's Memorial Playing Fields	Construct only	\$7.5m	Designer	Complete
				Builder	Q4 2020




Building Projects

Department for Correctional Services

Building Projects will be delivering over **\$164 million** of work across South Australian Prisons, including those already in construction:

- Yatala Labour Prison New Work (\$150M) (Managing Contractor).

No.	Project	Proposed delivery model	Project value	Contract	Anticipated procurement commencement
2.	Adelaide Women's Prison Gatehouse and Visits Centre Addition	Construct Only	\$12m	Designer	Complete
				Builder	Q3 2020
4.	Port Augusta Prison – Audio Visual Link (AVL) Upgrade [1]		Designer	Complete	
			Builder	Q3 2020	

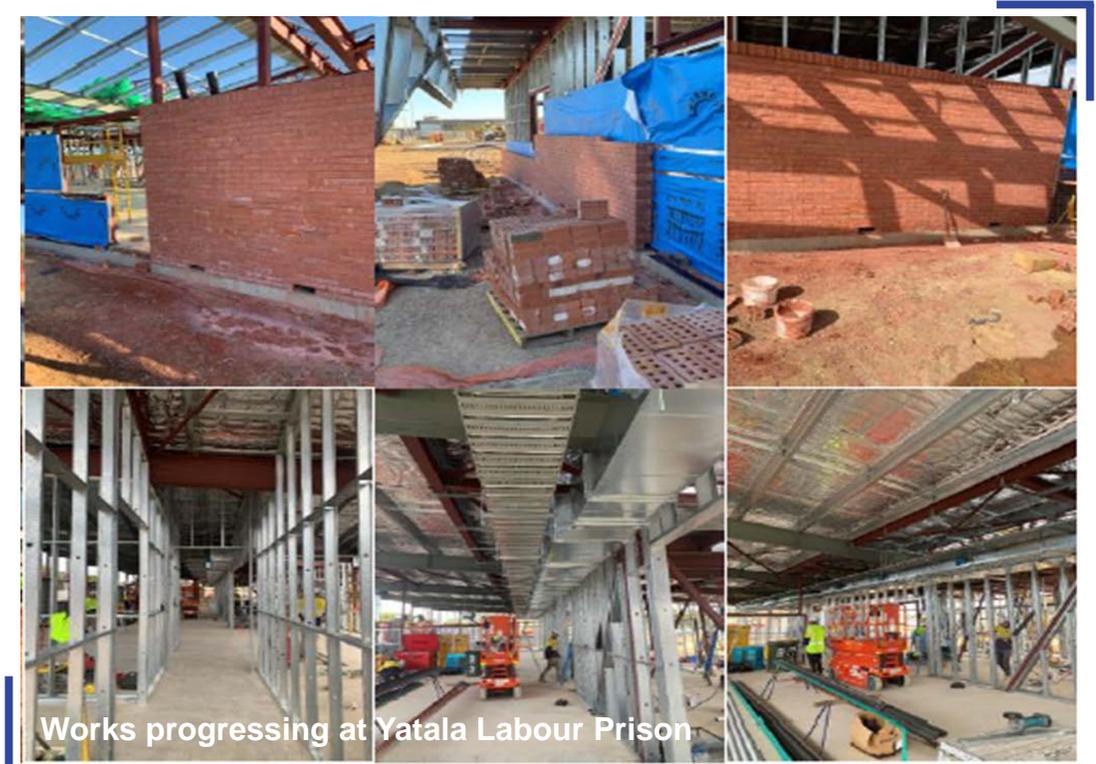

Works progressing at Yatala Labour Prison

[1] A COVID-19 AVL Stimulus program has been established to deliver 18 AVL suits across 5 prison sites. The program of works is being delivered by Building Projects, Facilities Services and Spotless.

Building Projects

Department for Environment and Water

Over the next 3-4 years DEW and the Department will collectively be delivering over \$50 million of projects as part of its Bushfire Recovery and Parks Renewal Program. These projects will include walking and bike trail construction, road and access track development, campgrounds and visitor facilities.

No.	Project	Proposed delivery model	Project value	Contract	Anticipated procurement commencement
1.	Nilpena Blacksmith's Shop	TBA	\$1.6m	Designer	Complete
				Builder	Q4 2020
2.	Parks 2025	TBA	\$6.4m	Designer	Q4 2020
				Builder	Q2 2021
3.	Future Major Capital Works Program (over 4 years)	TBA	\$5m	Designer	Q4 2020
				Builder	Q2 2021 (ongoing opportunities)
4.	Glenthorne National Park Establishment	TBA	\$7.2m	Designer	Q4 2020
				Builder	Q2 2021
5.	Kangaroo Island Bushfire Recovery	TBA	\$14	Designer	Q4 2020
				Builder	Q2 2021



Nilpena Blacksmith's Shop

Building Projects

Adelaide Cemeteries Authority

No.	Project	Proposed delivery model	Project value	Contract	Anticipated procurement commencement
1.	Enfield Memorial Park Multi-Function Community Precinct	Construct only	\$22.0m	Designer	Complete
				Builder	Q4 2020




South Australian Metropolitan Fire Service

No.	Project	Proposed delivery model	Project value	Contract	Anticipated procurement commencement
1.	Noarlunga MFS Command Centre	Construct only	\$6.5m	Designer	Q3 2020
				Builder	Q1 2021

Building Projects

Future Tender Program

For more information on upcoming building infrastructure tendering opportunities, please visit: https://dpti.sa.gov.au/building_projects

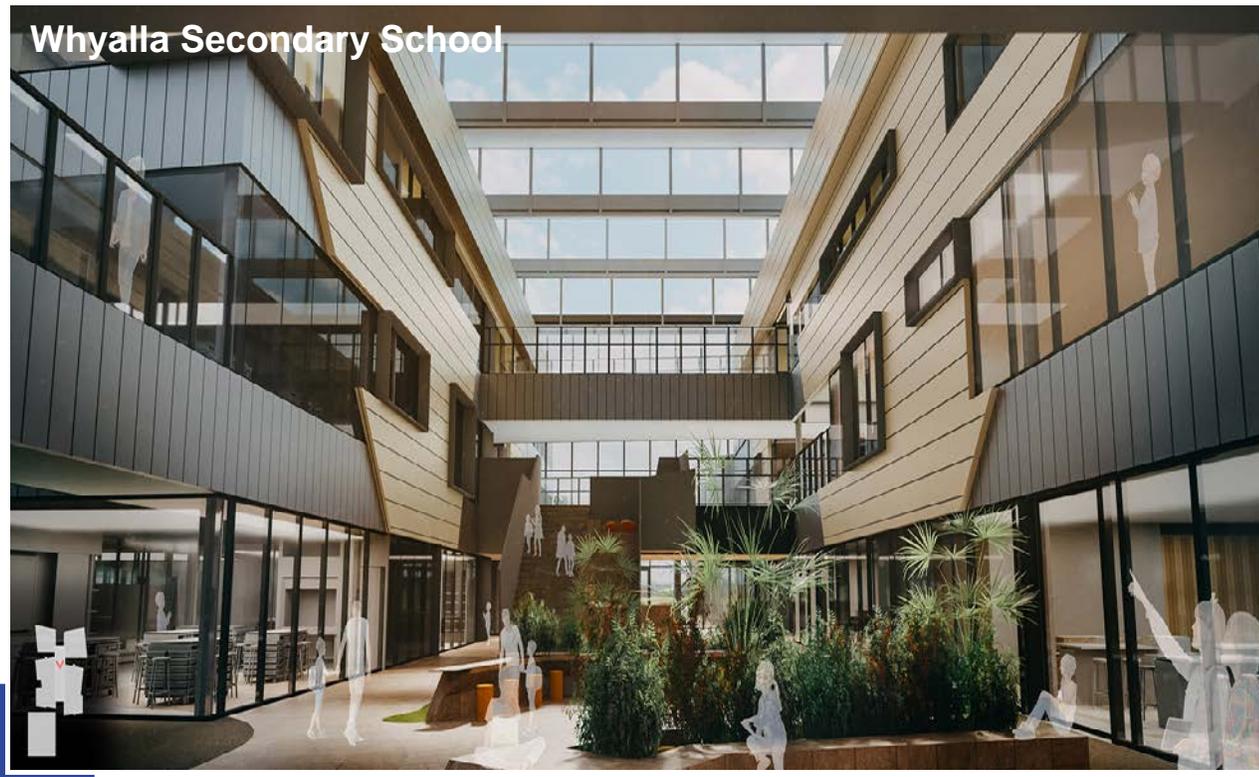

Forward Work Plan

Major Programs 2020-2023




**Download
a copy
today**



Government of South Australia

Department for Infrastructure
and Transport

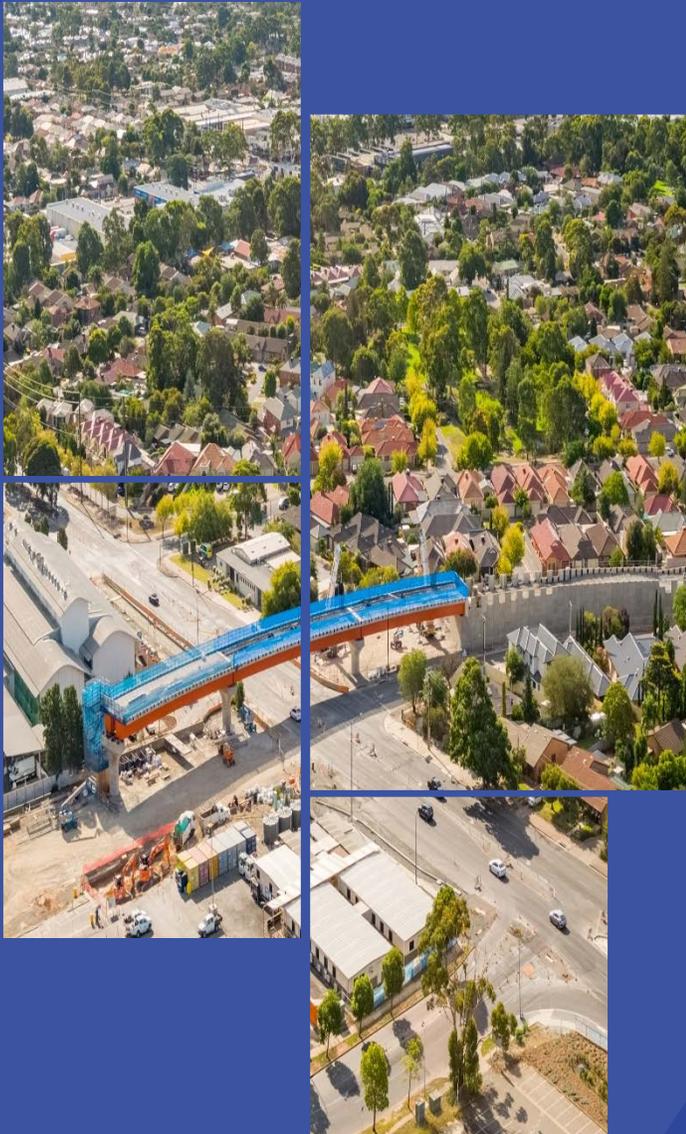

Thank you for your attendance

For further information, visit:

www.dpti.sa.gov.au
